



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 1



WORK ANTICIPATED NEXT 2 WEEKS APRIL 10 - APRIL 21

- Materials will be staged near the Phase 1 construction area
- Trash cans and benches will be removed within the Phase 1 area
- Businesses in the Phase 1 area are asked to remove planters and other decorative items on sidewalks by April 17
- The contractor will begin removing sidewalks the week of April 17

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" messages. To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code below



1

PHASE 1

April 17 - June 15

North side of St. Charles Road from Elizabeth Street to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main Street to Craig Place

3

PHASE 3


August 28 - October 29

South side of St. Charles Road from Elizabeth Street to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT



PROJECT MAP PHASE 1



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3

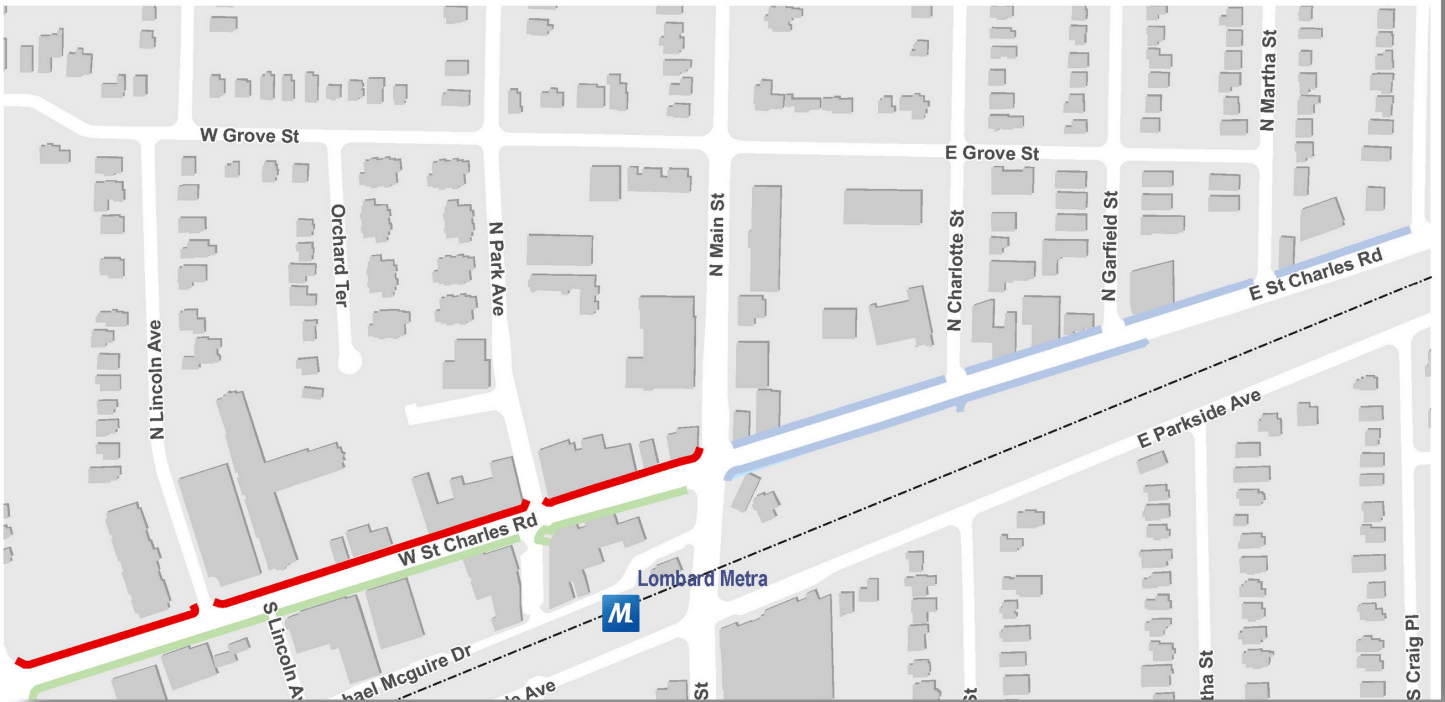

1

PHASE 1

April 17 - June 15

North side of St. Charles
Road from Elizabeth Street
to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main
Street to Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles
Road from Elizabeth Street
to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
