



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 1 - APRIL 21 UPDATE



WORK COMPLETED APRIL 10 - APRIL 21

- ✓ Trash cans and benches were removed within the Phase 1 area
- ✓ Placed construction barricades and other traffic control materials
- ✓ Began saw-cutting for pavement removal
- ✓ Completion of tree removal for Phase 1

WORK ANTICIPATED NEXT 2 WEEKS APRIL 24 - MAY 5

- Begin removal of sidewalks, curbs, and gutters
- Removal of tree vaults
- Installation of storm sewer and other drainage improvements

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text/email messages.

To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code.




REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT



PROJECT MAP PHASE 1



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3

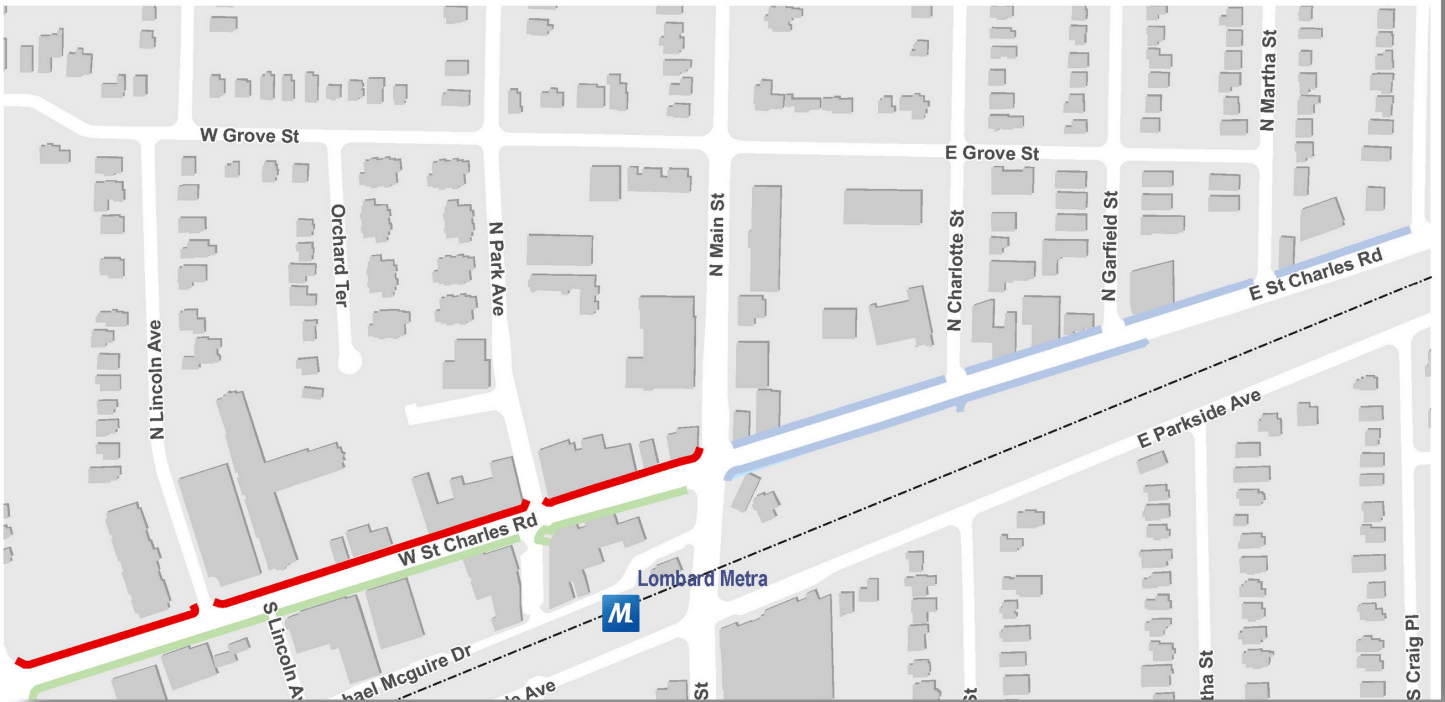

1

PHASE 1

April 17 - June 15

North side of St. Charles
Road from Elizabeth Street
to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main
Street to Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles
Road from Elizabeth Street
to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
