



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 1 - MAY 10 UPDATE



WORK COMPLETED APRIL 24- MAY 5

- ✓ Sidewalk, curbs, and gutters were removed in designated areas
- ✓ Tree vaults were removed
- ✓ Began Storm Sewer and other drainage improvements
- ✓ Began pouring concrete for sidewalks

WORK ANTICIPATED NEXT 2 WEEKS MAY 8 - MAY 19

- Ongoing installation of concrete for curbs and sidewalks
- Ongoing installation of storm sewer and drainage improvements
- Begin placement of brick pavers

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text/email messages.

To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT



PROJECT MAP PHASE 1



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3

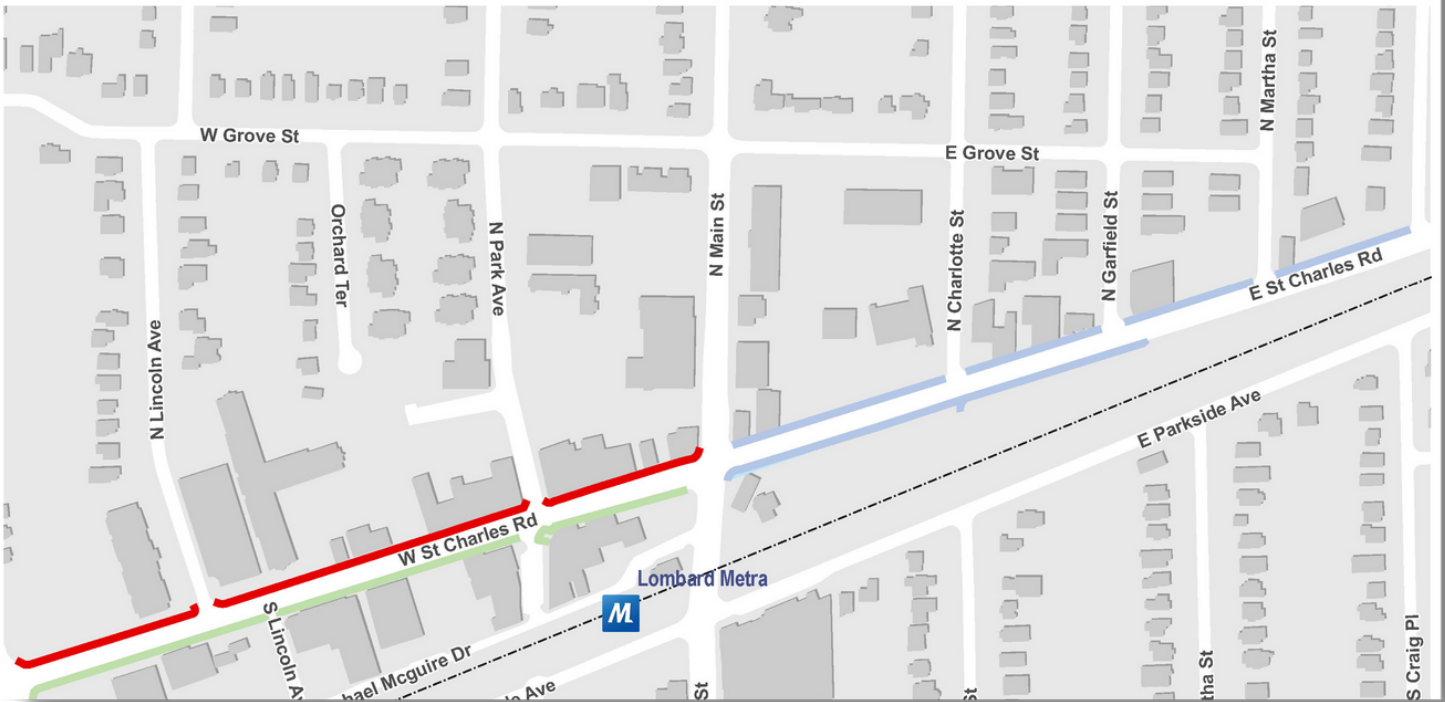

1

PHASE 1

April 17 - June 15

North side of St. Charles
Road from Elizabeth Street
to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main
Street to Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles
Road from Elizabeth Street
to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
