




DOWNTOWN SIDEWALK IMPROVEMENT PROJECT


PHASE 1 & 2 - JUNE 16 UPDATE

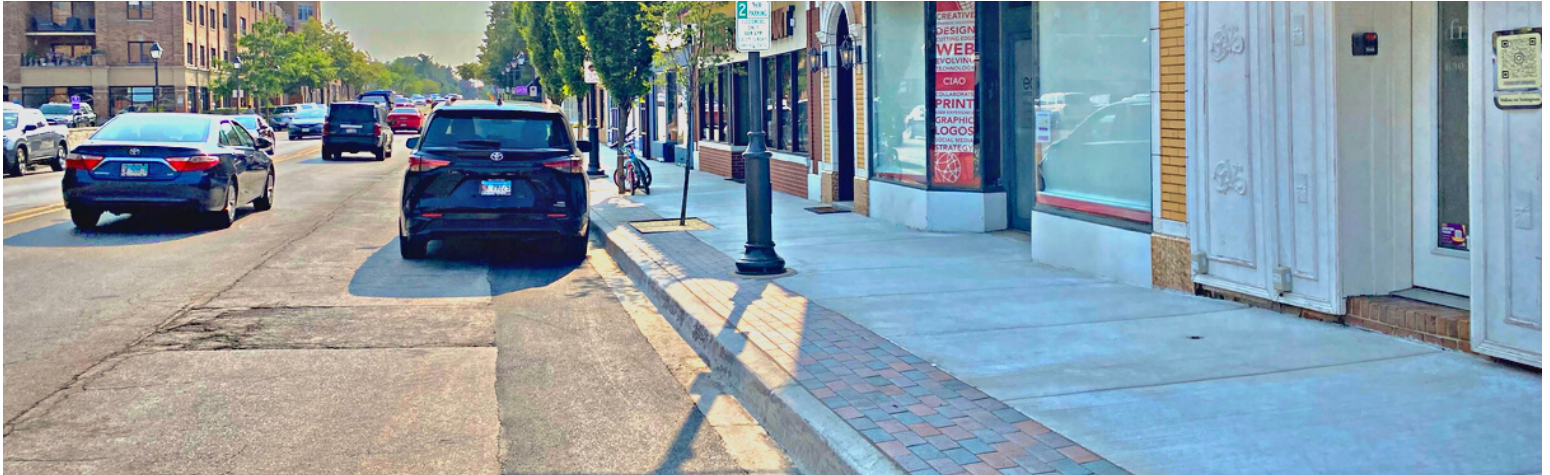

WORK COMPLETED
JUNE 5 - JUNE 16
PHASE 1



Substantial completion



WORK ANTICIPATED NEXT 2 WEEKS
JUNE 19 - JUNE 30
PHASE 2

- Ongoing sidewalk removal
- Installation of tree vaults and sidewalks
- Water valve replacements

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2




RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PROJECT MAP PHASE 1 & 2

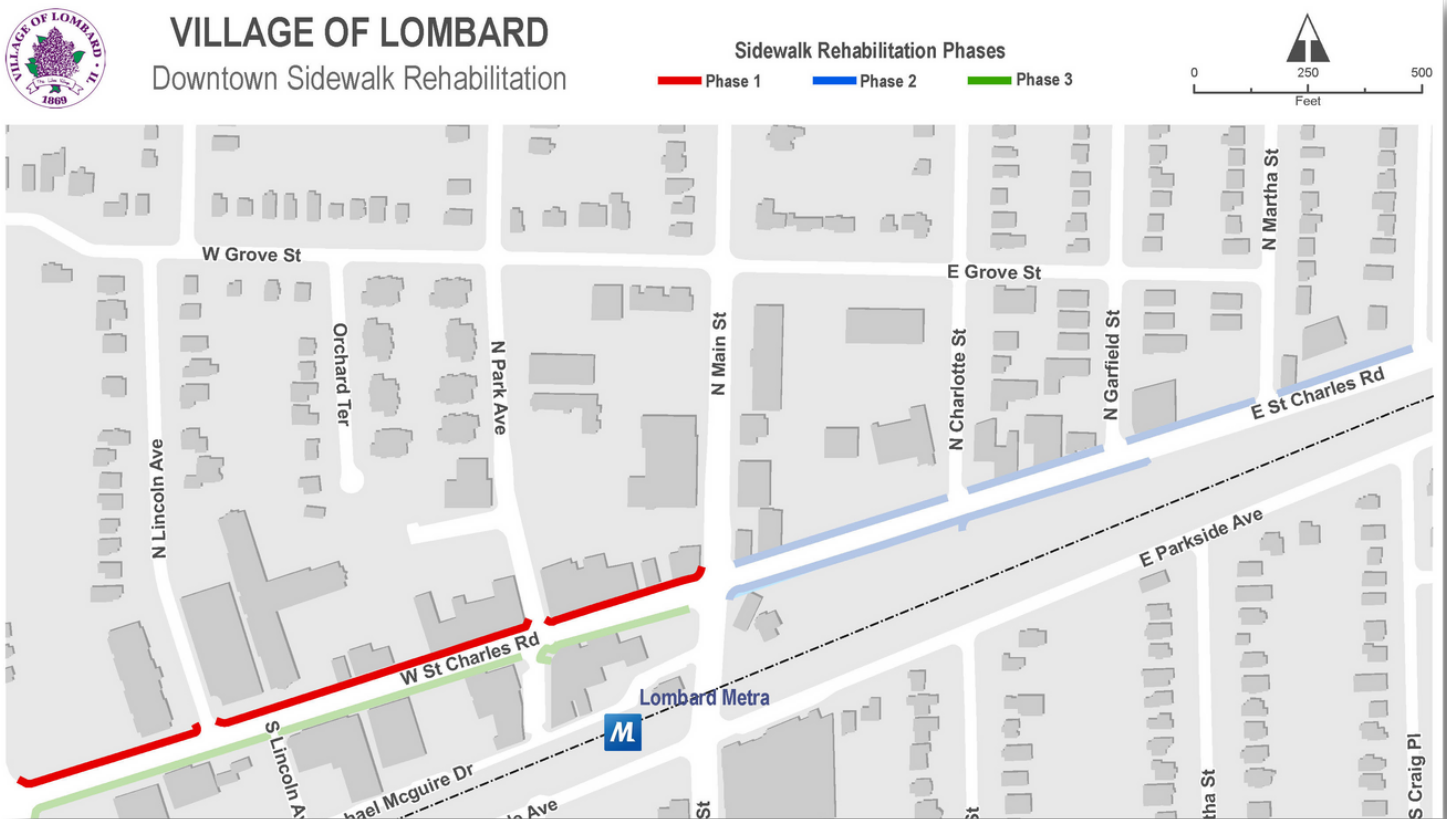

1

PHASE 1

April 17 - June 15

North side of St. Charles Road from Elizabeth Street to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main Street to Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles Road from Elizabeth Street to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
