



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 2 - JULY 18 UPDATE



WORK COMPLETED

JULY 3 - JULY 14

- Completed sidewalk removal on the north side
- Began pouring of concrete sidewalks, curb and gutter
- Completed storm sewer and drainage

WORK ANTICIPATED NEXT 2 WEEKS

JULY 17 - JULY 28

- Begin installation of brick pavers
- Complete placement of concrete sidewalks on the north side
- Complete installation of tree vaults

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2




RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PROJECT MAP PHASE 2

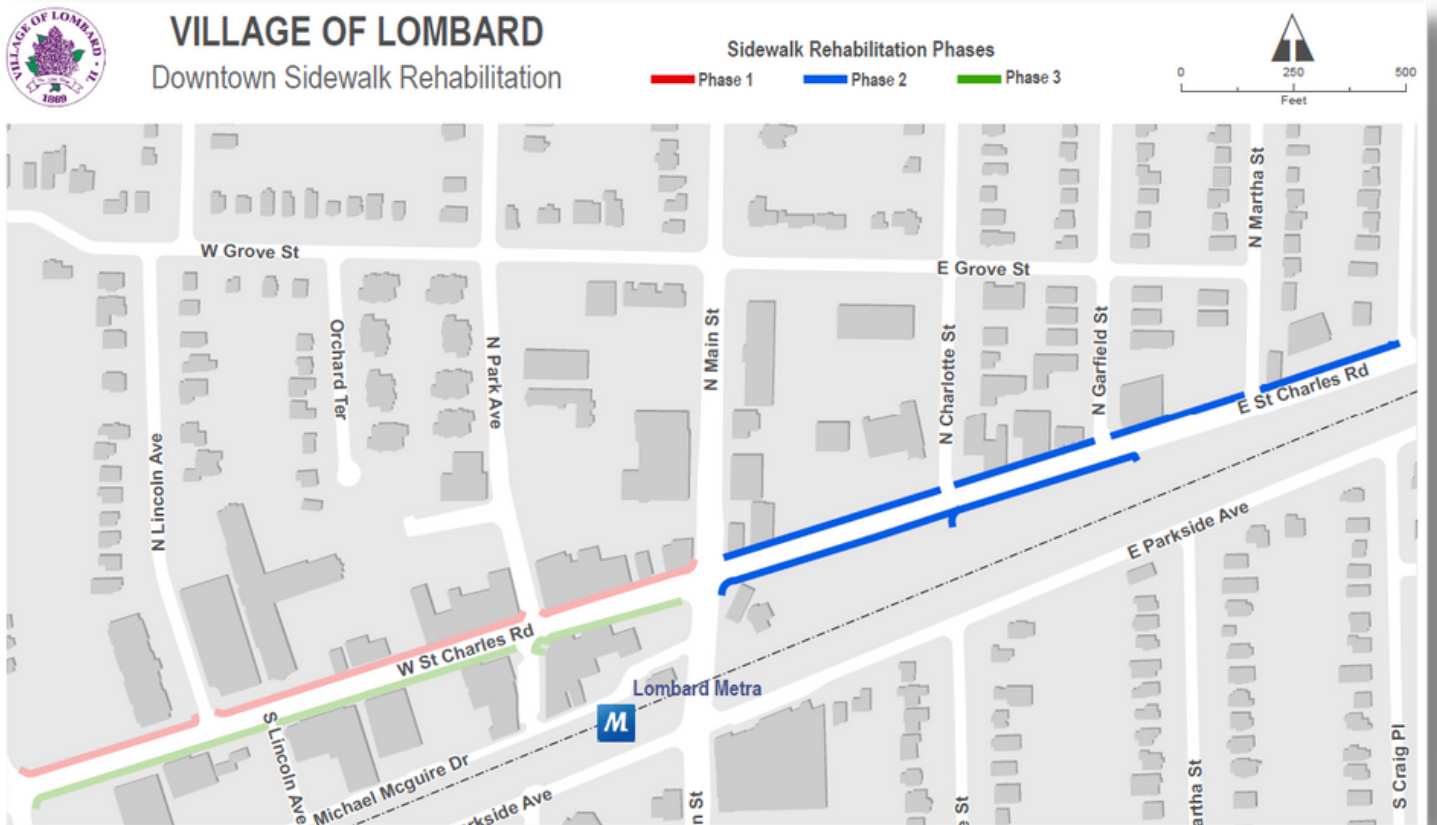

1

PHASE 1

April 17 - June 15

North side of St. Charles Road from Elizabeth Street to Main Street

2

PHASE 2

June 16 - August 27

St. Charles Road from Main Street to Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles Road from Elizabeth Street to Main Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
