



# DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 2 - JULY 31 UPDATE



## WORK COMPLETED JULY 17 - JULY 28

- Completed concrete placement on the north side
- Completed installation of tree vaults
- Began placement of new brick pavers on the north side

## WORK ANTICIPATED NEXT 2 WEEKS JULY 31 - AUGUST 11

- Complete placement of new brick pavers on the north side
- Relocate work zone to south side of St. Charles Road
- Remove and relocate temporary pavement markings to allow construction activities on south side
- Begin removal of sidewalk and concrete on south side

## STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

To sign-up for these updates, visit the Village website at [villageoflombard.org/sidewalkproject](http://villageoflombard.org/sidewalkproject) or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2




**RESIDENT ENGINEER**  
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP  
(248)756-2626; [MATT@THOMAS-ENGINEERING.COM](mailto:MATT@THOMAS-ENGINEERING.COM)

[WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT](http://WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT)



# DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

## PROJECT MAP PHASE 2

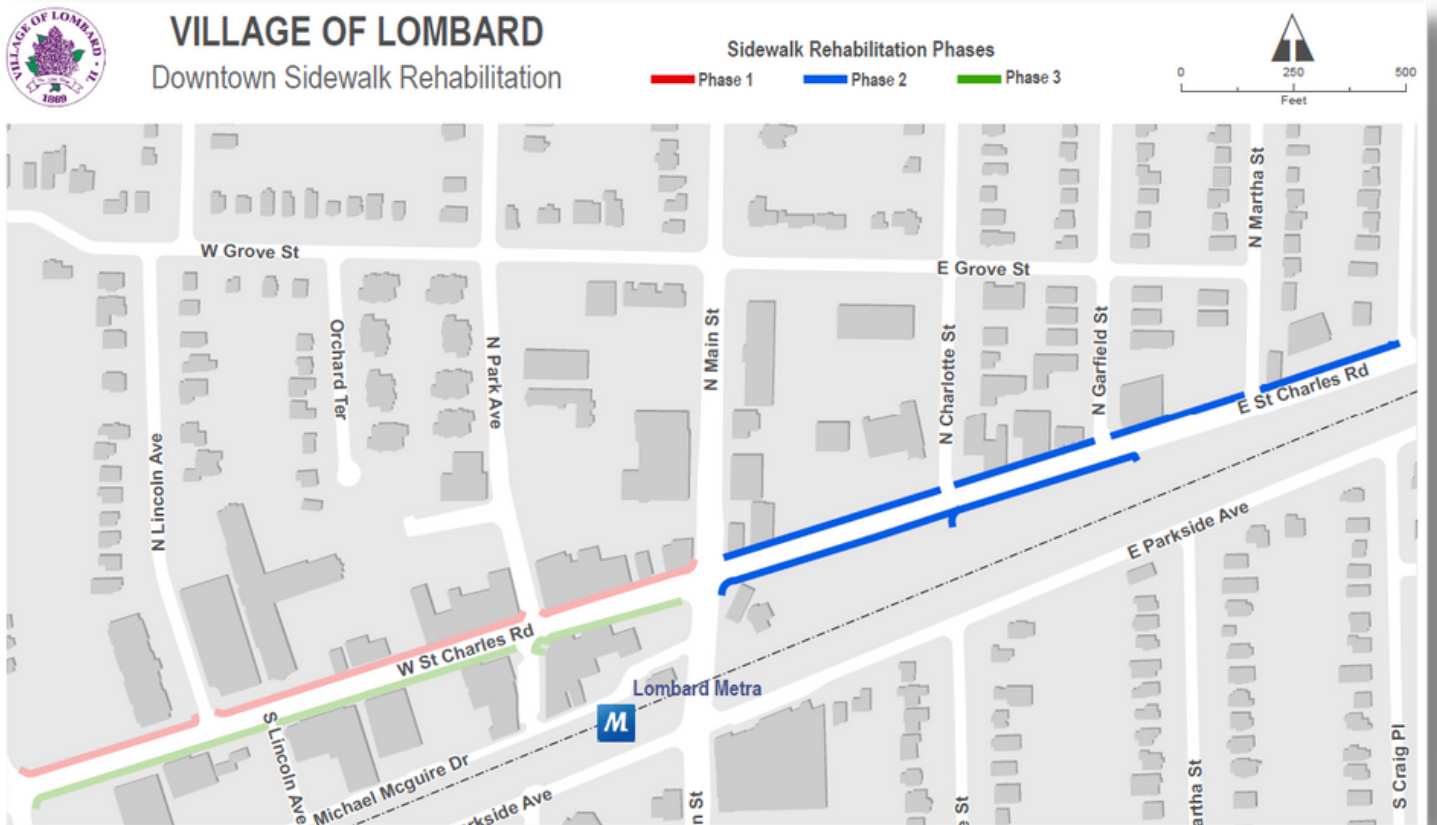

1

### PHASE 1

**April 17 - June 15**

North side of St. Charles Road from Elizabeth Street to Main Street

2

### PHASE 2

**June 16 - August 27**

St. Charles Road from Main Street to Craig Place

3

### PHASE 3

**August 28 - October 29**

South side of St. Charles Road from Elizabeth Street to Main Street



**RESIDENT ENGINEER**  
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP  
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

[WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT](http://WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT)
