



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 2 - AUGUST 14 UPDATE



WORK COMPLETED JULY 31 - AUGUST 11

- Completed placement of brick pavers on the north side

WORK ANTICIPATED NEXT 2 WEEKS AUGUST 14 - AUGUST 25

- Complete installation of roadway and pedestrian areas on the north side
- Install tree vault grates in Phase 1 & Phase 2 areas
- Substantial completion of Phase 2 sidewalks on the north side

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

To sign-up for these updates, visit the Village website at villageoflombard.org/sidewalkproject or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT


PROJECT MAP PHASE 2



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3

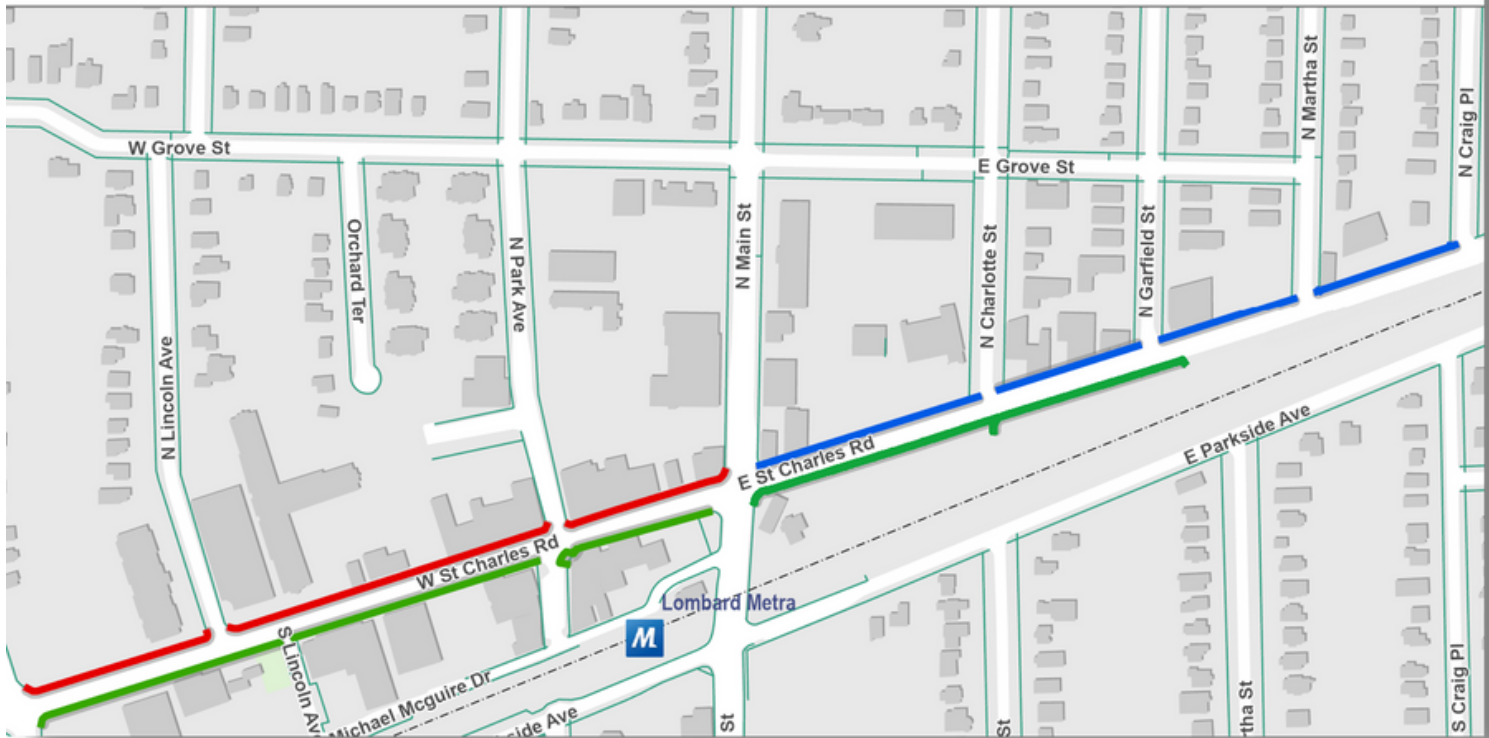

1

PHASE 1

April 17 - June 15

North side of St. Charles
Road from Elizabeth Street
to Main Street

2

PHASE 2

June 16 - August 27

North side of St. Charles
Road from Main Street to
Craig Place

3

PHASE 3

August 28 - October 29

South side of St. Charles
Road from Elizabeth Street
to Garfield Street



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
