



# DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 3 - SEPT 25 UPDATE



## WORK COMPLETED SEPTEMBER 11 – SEPTEMBER 22

- Traffic control barricades were placed along the south side of St. Charles Road
- Sidewalk was removed east of Main Street
- Pavement removal for storm sewer improvements

## WORK ANTICIPATED NEXT 2 WEEKS SEPTEMBER 25– OCTOBER 6

- Continued sidewalk removal
- Storm sewer improvements
- Water service box replacements
- Begin concrete curb installation

## STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

To sign-up for these updates, visit the Village website at [villageoflombard.org/sidewalkproject](http://villageoflombard.org/sidewalkproject) or scan the code.



REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2




**RESIDENT ENGINEER**  
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP  
(248)756-2626; [MATT@THOMAS-ENGINEERING.COM](mailto:MATT@THOMAS-ENGINEERING.COM)

[WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT](http://WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT)



# DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

## PROJECT MAP PHASE 3

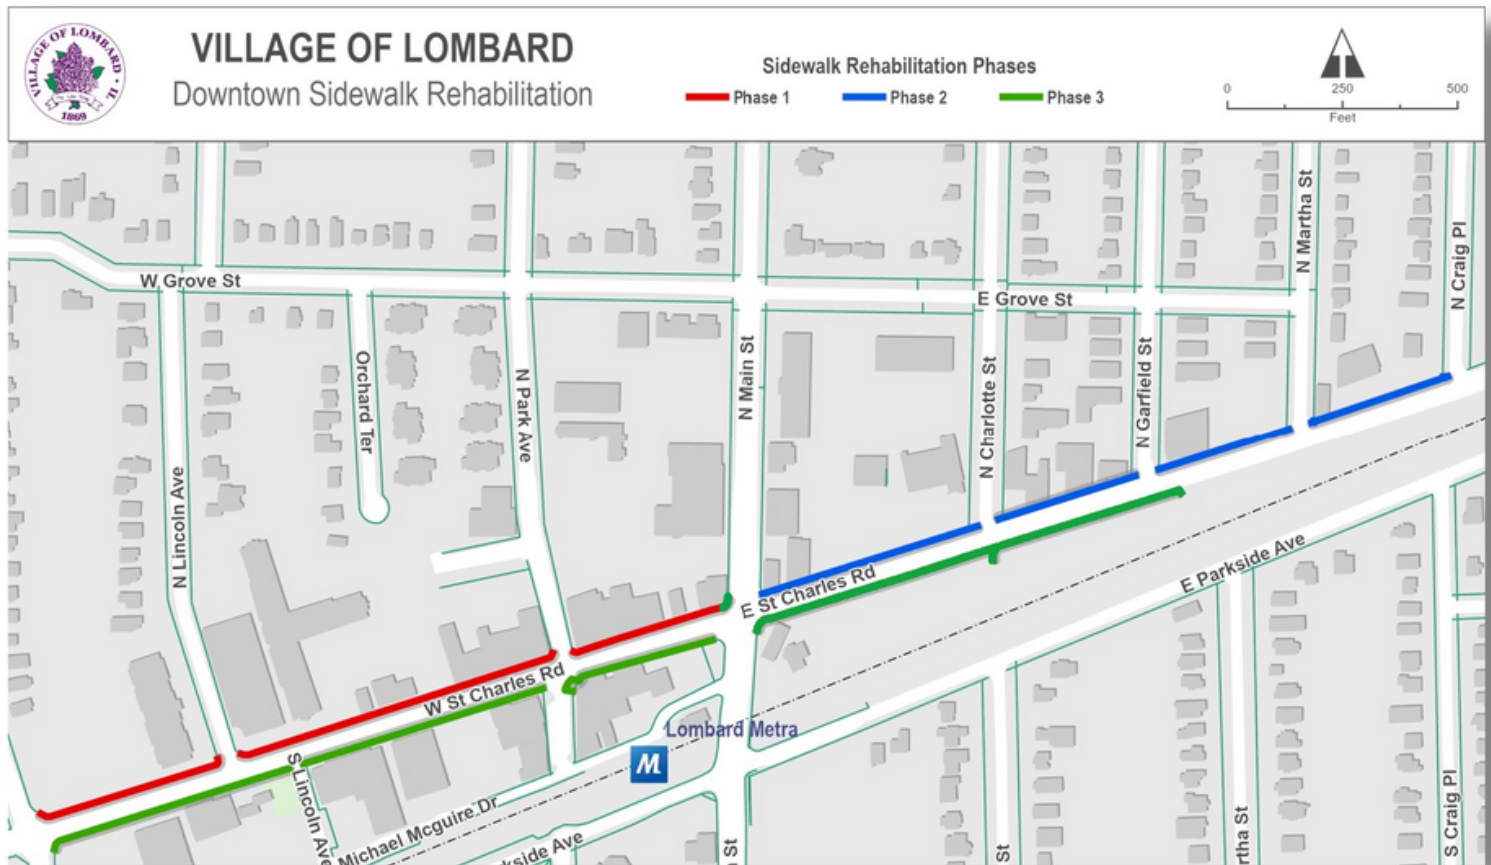

1

### PHASE 1

**April 17 - June 15**

North side of St. Charles  
Road from Elizabeth Street  
to Main Street

2

### PHASE 2

**June 16 - August 27**

North side of St. Charles  
Road from Main Street to  
Craig Place

3

### PHASE 3

**August 28 - October 29**

South side of St. Charles  
Road from Elizabeth Street  
to Garfield Street



**RESIDENT ENGINEER**  
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP  
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

[WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT](http://WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT)
