



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 3 & S. PARK- NOV 27 UPDATE



WORK COMPLETED NOVEMBER 6 – NOVEMBER 24

- Completed asphalt placement along St. Charles Road
- Substantially completed concrete work and brick paver installation along St. Charles Road
- Began removals on South Park Avenue
- Began storm sewer improvements on South Park Avenue
- Began and completed installation of new water main on South Park Avenue

WORK ANTICIPATED NEXT 2 WEEKS NOVEMBER 27 – DECEMBER 8

- Begin pedestrianization improvements at the northwest corner of St. Charles Road and Main Street
- Complete concrete work and brick paver installation along St. Charles Road
- Complete storm sewer improvements and sanitary sewer repairs on South Park Avenue
- Complete new water service installations to businesses on South Park Avenue
- Continue removals and begin concrete work on South Park Avenue

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

Sign up for these update at villageoflombard.org/sidewalkproject or scan the code.




REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PROJECT MAP


PHASE 3 & S. PARK AVE



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3 S. Park Ave

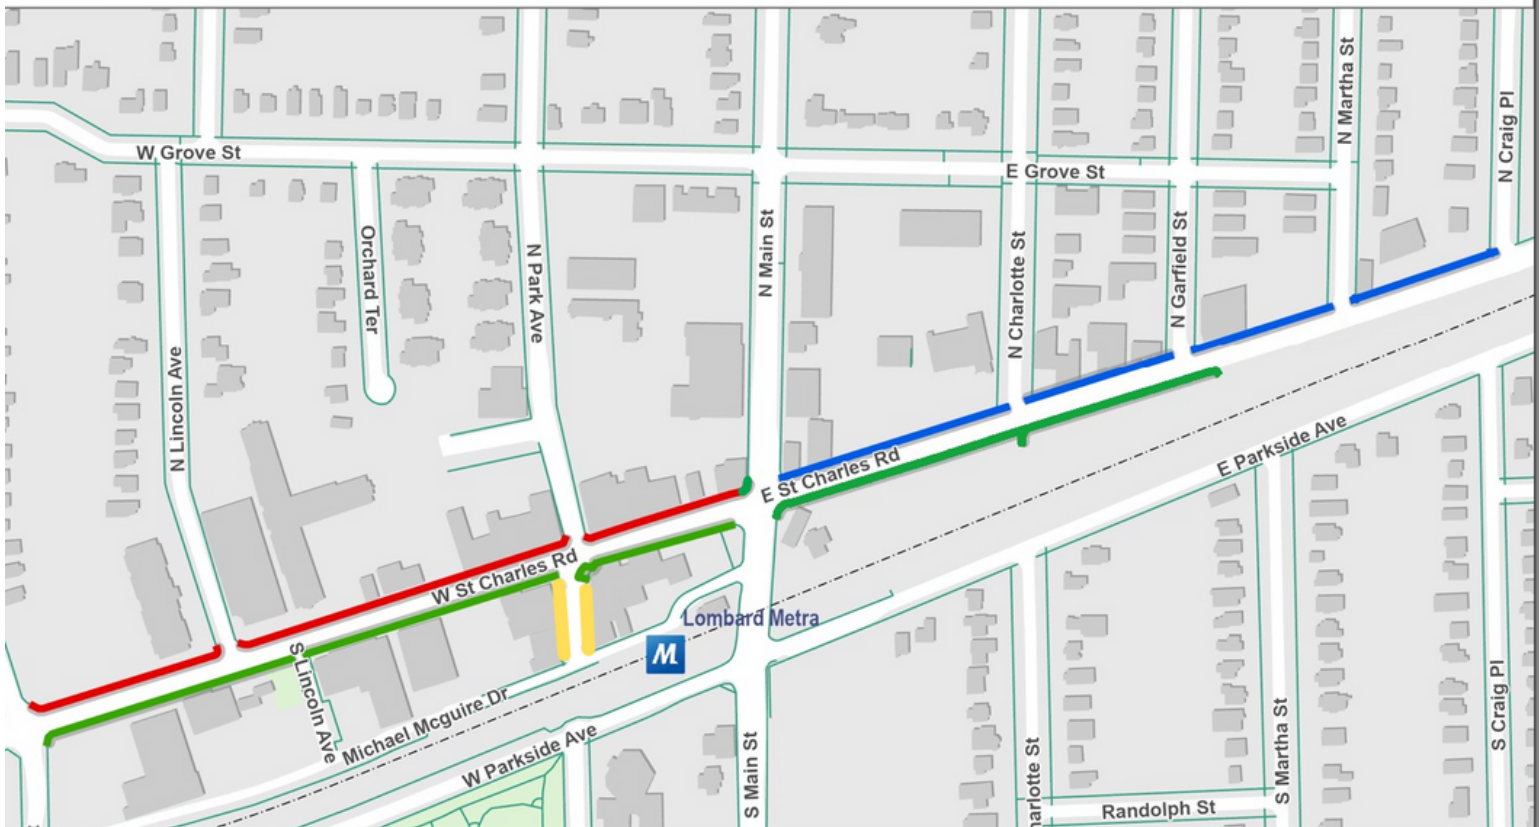

PHASE 1 & 2

April 17 - Aug 27

North side of St. Charles Road from Elizabeth Street to Craig Place

PHASE 3

Aug 28 - Nov 17

South side of St. Charles Road from Elizabeth Street to Garfield Street

S. PARK AVE

Nov 13 - Dec 29

S. Park Avenue from St. Charles Road to Michael McGuire Drive.



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATTC@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
