



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PHASE 3 & S. PARK- DEC 11 UPDATE



WORK COMPLETED NOVEMBER 27 – DECEMBER 8

- Completed concrete work along St. Charles Road
- Began the final brick paver installation at the northwest corner of Main Street and St. Charles Road
- Completed storm sewer improvements and sanitary sewer repairs on South Park Avenue
- Completed new water service installations to businesses on South Park Avenue
- Began concrete work on South Park Avenue

WORK ANTICIPATED NEXT 2 WEEKS DECEMBER 11 – DECEMBER 22

- Complete improvements along St. Charles Road
- Continue removals and concrete work on South Park Avenue
- Pour concrete roadway on South Park Avenue
- Begin sidewalk brick placement on South Park Avenue
- Begin installation of lighting and traffic signal improvements

STAY INFORMED

The Village will issue project updates through an online e-newsletter and "notify me" text or email messages.

Sign up for these update at villageoflombard.org/sidewalkproject or scan the code.




REFER TO PROJECT SCHEDULE AND MAP ON PAGE 2



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT



DOWNTOWN SIDEWALK IMPROVEMENT PROJECT

PROJECT MAP


PHASE 3 & S. PARK AVE



VILLAGE OF LOMBARD
Downtown Sidewalk Rehabilitation

Sidewalk Rehabilitation Phases

Phase 1 Phase 2 Phase 3 S. Park Ave

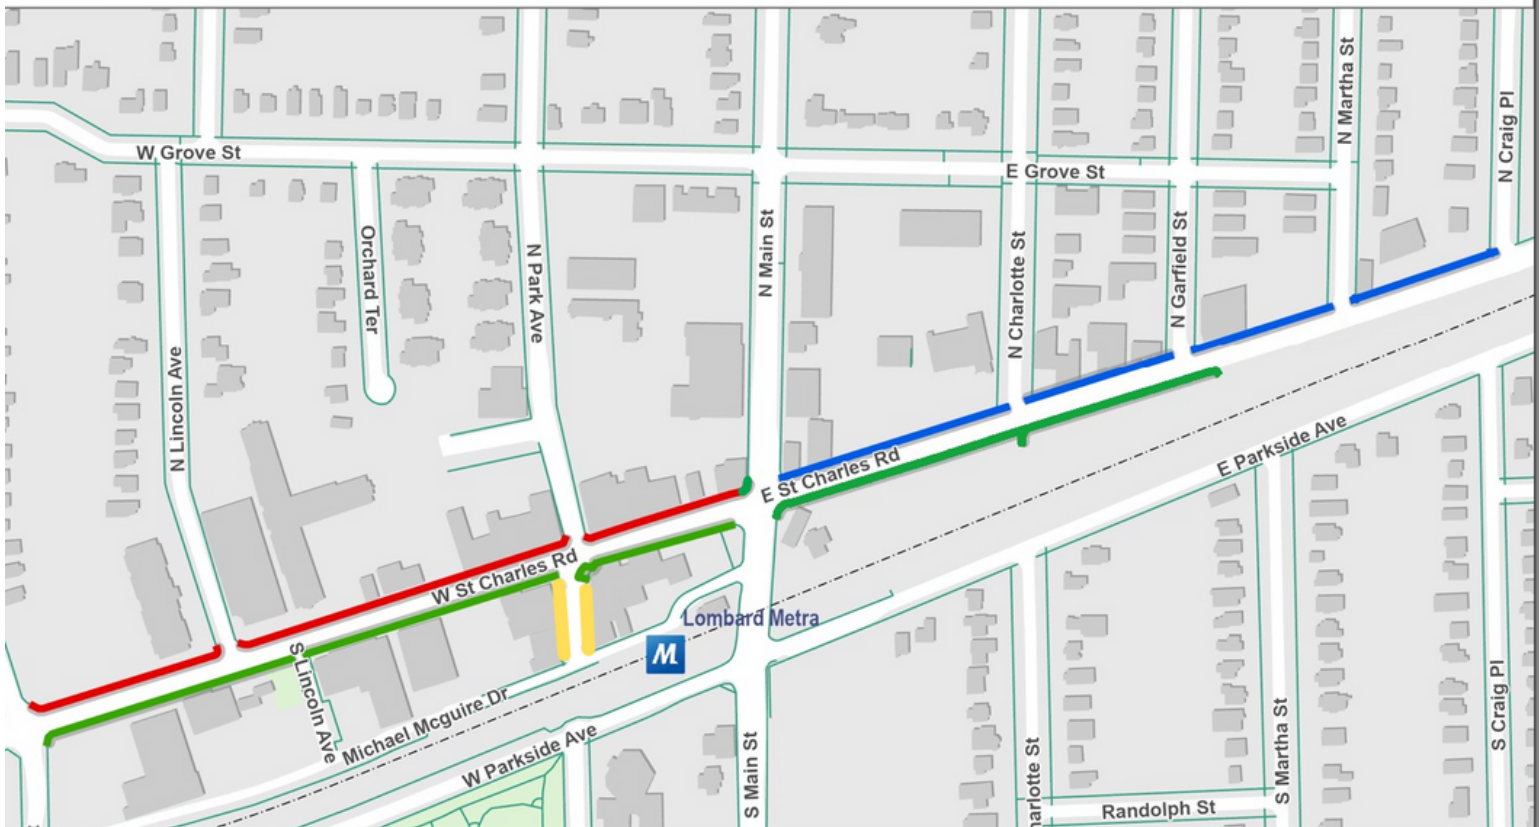

PHASE 1 & 2

April 17 - Aug 27

North side of St. Charles Road from Elizabeth Street to Craig Place

PHASE 3

Aug 28 - Nov 17

South side of St. Charles Road from Elizabeth Street to Garfield Street

S. PARK AVE

Nov 13 - Dec 29

S. Park Avenue from St. Charles Road to Michael McGuire Drive.



RESIDENT ENGINEER
MATT CHAMPINE, PE - THOMAS ENGINEERING GROUP
(248)756-2626; MATT@THOMAS-ENGINEERING.COM

WWW.VILLAGEOFLOMBARD.ORG/SIDEWALKPROJECT
